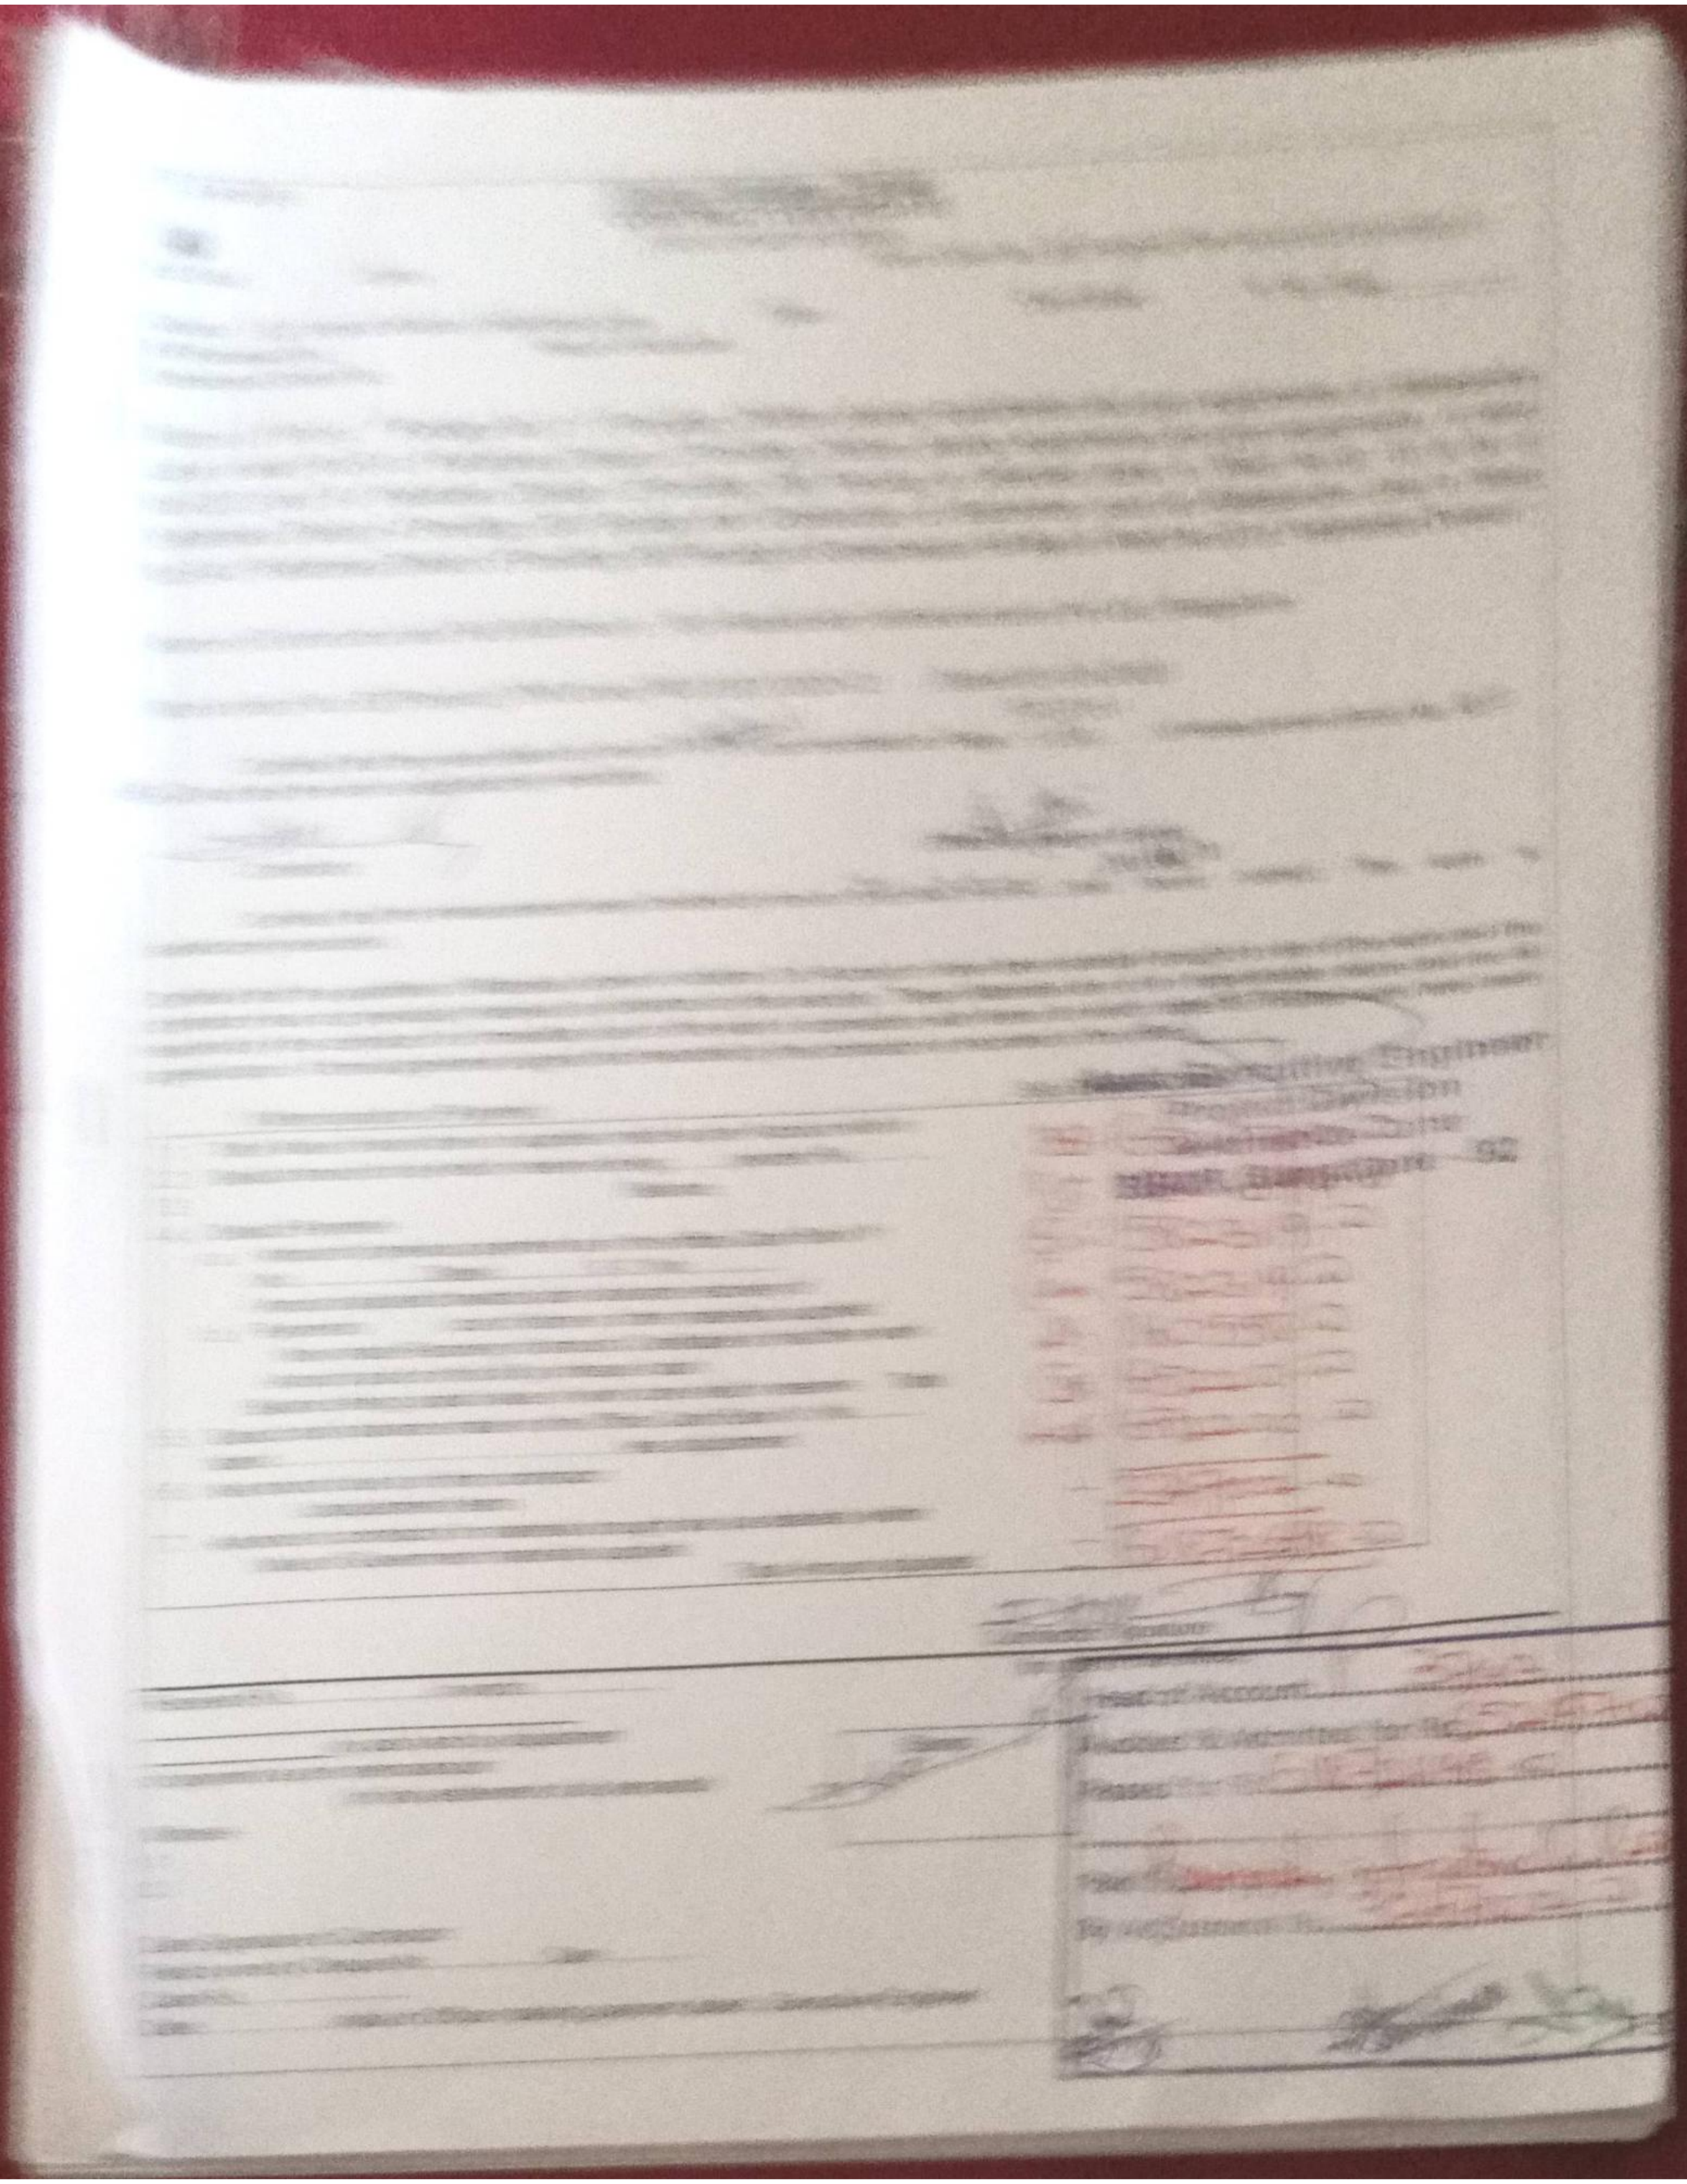

Scanned by TapScanner

Providing Children playing equipments and gym equipments at Allalasandra Lake in ward No.04 of Yelahanka Division 2.Providing Children playing equipments and gym equipments in ward No.02,03 and 04 Yelahanka Division 3.Providing Grill Fencing to Selected parks in Ward No.02, 03 & 04 of Yelahanka Division 4.Providing Grill Fencing and Construction of Badminton court at Allalasandra Lake in Ward No.04 of Yelahanka Division 5.Providing Grill Fencing at Someshwara Hill lake in Ward No.03 of Yelahanka Division

Sl No	Description of Work	Unit	Tender Quantity	Previous Measurement			Present Measurement			Total Upto Date		Remarks
				Quantity	Rate	Amount	Quantity	Rate	Amount	Quantity	Amount	
1	Removing and resetting of kerb stones. complete as per specifications and directions of the Engineer in charge.	m	2253.28	0.00	105.88	0.00	807.15	105.88	85481.04	807.15	85481.04	
2	Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including cost of materials, labour charges of machinery, loading and unloading, lead and lift, transportation etc., complete as per specifications and directions of the Engineer in charge.	m	3934.00	0.00	436.98	0.00	558.58	436.98	244086.10	558.58	244086.10	
3	Providing and fixing M.S. Block pipe of 38mm dia, of heavy guage of 14 including removing the bends, cutting the pipe, and fixing pipe in between the existing two verticle poles (M.S. rectangular poles) and spot welding the chain link with M.S. block pipe including cost of all materials wastage in cutting, and scaffolding wherever necessary with all lead and lift as directed by the Engineer-in-charge of work etc., complete including two coats of approved quality paint over one coat of shop paint complete as per specifications and directions of the Engineer in charge.	m	432.00	0.00	436.98	0.00	0.00	436.98	0.00	0.00	0.00	
4	Providing and laying in position plain cement concrete of mix 1:3:6 with OPC cement @ 220kgs, with 40mm and down size graded granite metal coarse aggregates @0.892cum and fine aggregates @ 0.465cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation including cost of all materials, labour, HOM of machinery, curing complete as per specifications. complete as per specifications and directions of the Engineer in charge.	Cum	157.27	0.00	5563.25	0.00	152.15	5563.25	846459.08	152.15	846459.08	
5	Providing and applying painting in two coat with Synthetic enamel paint of approved brand and manufacture on concrete surface with cost of materials ,labour ,complete as per specifications.complete as per specifications and directions of the Engineer in charge.	Sqm	1925.30	0.00	85.68	0.00	384.86	85.68	32967.11	384.86	32967.11	
6	Providing and laying heavy duty cobble stones 60mm thick interlock pavers,using cement and course sand for manufacturer of blocks of approved size,shape and colour with a minimum compressive strength of 281 kg per sqm over 50mm thick sand bed(average Thinkness) and compacting with plate vibrator having 3 tons compaction force thereby forcing part of sand underneath to comeup in between joints , final compaction of pavers surfaces joint into its final level including cost of materials,labour and HOM complete as per specifications. complete as per specifications and directions of the Engineer in charge.	Sqm	1902.74	0.00	1128.05	0.00	476.36	1128.05	537359.31	476.36	537359.31	
7	KSRRB M200-12.2. Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work, including T&P and scaffolding wherever necessary, sorting the dismantled material, disposal of unserviceable material and stacking the serviceable material with all lifts complete as per specifications. i) Lime /Cement Concrete. I. By Manual Means :B. Cement Concrete Grade M-15 & M-20. MORTH Specification. (5km lead = 57+2*1.28X5). complete as per specifications and directions of the Engineer in charge.	Cum	2.85	0.00	667.01	0.00	0.00	667.01	0.00	0.00	0.00	
8	Dismantling of barbed wire fencing / wire mesh fencing including posts, foundation concrete, back filling of pit by manual means including disposal of dismantled material with all lifts and stacking serviceable material and unserviceable material separately complete as per specifications. MORTH Specification. complete as per specifications and directions of the Engineer in charge.	m	1015.70	0.00	71.23	0.00	958.20	71.23	68252.59	958.20	68252.59	

Scanned by TapScanner

	complete as per specifications and directions of the Engineer in charge.	cum	432.61	0.00	4923.19	0.00	274.82	4923.19	1352988.51	274.82	1352988.51	
10	Providing and constructing granite / trap / basalt size stone masonry in superstructure with cement mortar 1:4 , edges of stones chistle dressed in courses not less than 15 cms high, bond stones at two m. apart in each course including cost of materials, labour, scaffolding, curing complete as per specifications complete as per specifications and directions of the Engineer in charge.	Cum	299.94	0.00	6432.39	0.00	189.45	6432.39	1219609.05	189.45	1219609.05	
11	Providing ruled pointing to coursed stone masonry with cement mortar 1:3, 20mm deep, after raking joints to depth of 20mm nicely lining, including cost of materials, labour, curing complete as per specifications. complete as per specifications and directions of the Engineer in charge.	Sqm	589.02	0.00	152.08	0.00	267.17	152.08	40630.45	267.17	40630.45	
12	Providing and laying in position plain cement concrete of mix M20 with OPC cement @ 300kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregtes @ 0.43cum, with superplastisiser @3lts confirming to IS9103-1999 Reaffirmed-2008, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, including cost of all materials, labour, HOM of machinery, curing complete as per specifications complete as per specifications and directions of the Engineer in charge.	Cum	126.16	0.00	5707.83	0.00	65.72	5707.83	375094.03	65.72	375094.03	
13	Supplying and fixing M.S rectangular poles made out of two equal angles of 65X65X6 mm welded together and fixed in CC 1:2:4 with two numbers 16mm dia M.S hold fast rods each of length 25cms including cost of all materials cutting, bending scaffolding whereever necessary, nicely finishing the welded jonts with all lead lift and as per the direction of engineer incharge of the work and including providing two coats of approved quality paint over coat of shop painting (excluding cost of earthwork and concrete) .complete as per specifications and directions of the Engineer in charge.	m	646.04	0.00	920.15	0.00	0.00	920.15	0.00	0.00	0.00	
14	Fabricating providing and erecting in position of MS Hot Dip galvanized sq hallow poles of 132 x132 heavy gauge length 3000mm with MS Hot Dip galvanized grill work as per approved design and drawing of chief architect using 12 x75mm galvanized flat for alround frame and 20 x 20mm galvanized forged ornamental arrow head in top and buttom the work is inclusive of throughing flat square rods placing welding all the joints including griding finishing 2 coats of anticorrossive paint over one coat of metal primer the rate is inclusive of all materials all items of work cost painting welding cutting griding with lead and lift as per specifications including loading and unloading with cost and conveyance of all materials labour machinery and incidental charges for the successful completion of the work as per direction of engineer in charge of work.	Sqm	2418.00	0.00	9240.96	0.00	2121.08	9240.96	19600769.23	2121.08	19600769.23	
15	Providing chain link fencing 50mm size of 8 guage properly stretched between rectangularpoleas and fixed with suitable bolts & nuts, the free ends shall be welded to the pole and block pipe at top and bottom as required including cost of all materials, labour lead and lift and as per the directions of the engineer incharge of work including two coats of approved quality paint over one coat of shop paint. completion of the work as per direction of engineer in charge of work.	Sqm	1131.31	0.00	560.19	0.00	0.00	560.19	0.00	0.00	0.00	
16	Providing and fixing M.S Gate as per Chief Architect Drawing , using 50mm x 50mm x 14 gauge M.S hollow pipe frame work bent to ornamental shape as shown in the drawing and 35mm x 6mm and 16mm x 16mm Square rods for verticals alternatively spaced at 4cms c/c in two halves and 40 mm x 6mm M.S flats for horizontal member and at the top cast iron spikes are provided at alternate vertical members as shown in the drawing etc., complete. all the steel surface should be throughly cleaned free of rust and painted with anti materials , labour charges for all items of work , Hire charges for welding , cutting and grinding eqipment , electricity charges , with lead and lift , loading and unloading charges , etc.completion of the work as per direction of engineer in charge of work.	Sqm	27.90	0.00	3226.30	0.00	0.00	3226.30	0.00	0.00	0.00	

Scanned by TapScanner

17	at 150mm c/c ...as shown in the drawing including providing hot dip galvanized forged ornamental design in between rods and leads at top, middle and bottom, intermediate supports of 75x12mm and 50x6mm arch heat to hot dip galvanized flats.The work is inclusive of thereighing GI, Flat GI Sqm. rods, placing, welding all the joints including grinding, finishing metal putty, painting two coats enamel painting. The rate is inclusive of all materials Like GI Sq. GI Pipe, GI Forged designs etc., heavy duty hinges are made out of 75mm solid sq. block assembled with 20mm dia bearing in three places for each flap. Heavy duty locking arrangement of low places including cost of labour, painting, erection charges using hoist pulley cranes, with all lead and lift, loading, trasportation, unloading, scaffolding charges and all other completion of the work as per direction of engineer in charge of work.	Sqm	56.40	0.00	12696.80	0.00	67.50	12696.80	15212.16	67.50	15212.16	
18	Providing and applying enamel metal paint two coats (exclusive primer coat) over new steel or other metal surfaces brushing to give an even shade after cleaning oil grease dirt and other foreign matters including cost of materials labour complete as per specifications completion of the work as per direction of engineer in charge of work.	Sqm	839.71	0.00	151.06	0.00	0.00	151.06	0.00	0.00	0.00	
19	PROVIDING TRAPEZOIDAL PROFILED SHEET Providing and installing of pre painted Galvalume iron Trapezoidal profiled sheet of approved make 1060 mm width (1000 mm cover width), 28-30 mm crest height with crest distance of 200 mm c/c with 2 ribs at the centre for stiffening. The total coated thickness (TCT) of the sheet will be 0.47 mm +/- 0.02 mm tolerance Zinc-Alu Alloy coating AZ150 gsm as per ASTM 1397/A755-550 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 20-22 microns using self drilling self tapping screws of 25 mm length, to be fixed over the existing purlins, rafters, channels and trusses,completion of the work as per direction of engineer in charge of work.	Sqm	143.23	0.00	708.91	0.00	98.47	708.91	101532.19	98.47	101532.19	
20	Earthwork excavation By manual means for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in ordinary soil not exceeding 1.5 m in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. after breaking of clods complete as per specifications. (5km lead = 57+2*1.28X(5), completion of the work as per direction of engineer in charge of work. (Qty upto 125%)	Cum	589.99	5.00	390.78	0.00	737.48	390.78	288154.75	737.48	288154.75	
	Qty Above 125%						16.98	390.78	6636.74	16.98	6636.74	
21	Providing and filling sand in trenches to required depth including watring ramming with all leads and lift complete as per specifications and directed by the engineer incharge at the site completion of the work as per direction of engineer in charge of work.(Qty upto 125%)	cum	285.00	0.00	2206.05	0.00	366.25	2206.05	79800.01	366.25	79800.01	
	Qty Above 125%						9.63	2206.05	149179.40	9.63	149179.40	
22	Providing and constructing load bearing wall with solid concrete blocks of size 400x200x200 mm having block density not lessthan 1800 kg/m3 and having a minimum average compressive strength 5.00 N/mm2 confirming to IS 2185 (Part) 2005 and constructed with CM 1:4 , as per IS 2572:2005 including cost of all materials, labour charges, scaffolding, curing complete as per specifications completion of the work as per direction of engineer in charge of work.	Sqm	182.60	0.00	979.94	0.00	90.30	979.94	98277.98	90.30	98277.98	
23	Providing and laying fixing cement base, precast, pre polished cement concrete, designer tiles 25mm thick for flooring conforming to IS 1237 heavy duty tiles for flooring, treads of steps and landing, laid on a bed of 12mm thick cement mortar 1:3 mix finished with flush pointing using white cement, including cost of materials, mortar including cutting, grinding the edge to half/full round wherever required, labour, curing complete as per specifications completion of the work as per direction of engineer in charge of work.(Qty upto 125%)	Sqm	111.54	0.00	1319.59	0.00	130.42	1319.59	103691.35	130.42	103691.35	
	Qty Above 125%						24.30	1319.59	25855.07	24.30	25855.07	

Scanned by TapScanner

Sl No	Description of Work	Unit	Quantity	Quantity				Rate	Amount	Quantity	Amount	Remarks
24	Supply & fixing of children multi play equipment with spiral slide, monkey bar with number pannel Upright structural posts of height 4.2 m are to be hot dip galvanized steel with a 114 mm OD and 2.2mm wall thickness of tubing Roof of size 1.9m x 1.7m x 0.77 m , spiral slide of size2.56m x 1.85m x 2.68m. Top rails of monkey bar size 1.8m x 1.3m are all robotic welded & fabricated from 48mm OD galvanized steel pipes for the outer bars &32 mm OD galvanized steel for the inner parallel bars with a baked on powder coated finish. Deck of size 1.45 x 1.45 m are pressed and punched , welded ,sand blasted ,powder coated to 2.2mm thickness or vinyl coated to a thickness of 4mm Deck of size 1.45 x 1.45 m are pressed and punched , welded ,sand blasted ,powder coated to 2.2mmthickness or vinyl coated to a thickness of 4mm. Deck, step, platform ,stairs, baffle shall be all robotic welded. Inclined ramps of size 1.92m x 0.65m , stair case of size 1.5m x 0.77m are fabricated from solid 2mm perforated solid punched steel Frisbee climber , piped walls of size 1 m are robotic welded , fabricated from 32 mm OD galvanized steelpipes for outer and 25mm OD galvanized steel pipes for inner bar with baked on powder coat finish.The poles welded on to base plate made from steel with 114mm inner dia double slide of size 2.2 m x 1.5m x 1.45 m panel. The rates are to be inclusive of supply and installation at site. Inclusive of All Taxes and Transportation Charges. completion of the work as per direction of engineer in charge of work.	Each	2.00	0.00	1936256.44	0.00	2.00	1936256.44	3872512.88	2.00	3872512.88	
25	Supply and fixing of childern Multi Play Equipment with double swing, curved side toddler slide with animated roof Upright structural posts of height 2.7 m and 3 m are to be schedule HOT DIP Galvanized steel with a 114mm OD and 2.2mm (wall) thickness of the tubing. The poles are welded on to a base plate made from steel with 114mm inner diameter. Deck of size 1.45 x 1.45m and Staircase of size 1.48 m x 0.60 m are fabricated from 2mm perforated solid punched steel. Deck perimeter is precision pre punched for attachments. Handrail of height 1.90 m and Dia 32 mm shall be an all-robotic welded unit, fabricated from 32 O.D. galvanized steel pipes with a baked on powder coating finish. Exposed hardware shall be covered with ultra violet stabilized plastic safety caps as per Sun Roof of size 2.0 m x 1.78 m x 0.77m, Spiral Slide of size 2220 mm x 1630 mm x 1880 mm , Straight Slide of size 1645 mm x 800 mm x 1140 mm, Panels. Roofs and panels are copyrighted and IP protected worldwide. Spring Climber of thickness Dia 38 mm, 3 step ladder , Frisbee Climber ,Piped walls of Height 2.7 m are all robotic welded fabricated from 32 O.D. galvanized steel pipes for the outer pipes and 25mm O.D. galvanized steel for the inner parallel bars with a baked on powder coat finish. The rates are to be inclusive of supply and installation at site. Inclusive of All Taxes and Transportation Charges. Charges. completion of the work as per direction of engineer in charge of work.	Each	1.00	0.00	1229647.65	0.00	1.00	1229647.65	1229647.65	1.00	1229647.65	
26	Supply and fixing of childern Multi Play Equipment with curved slide and number panel Upright structural posts of height 2.4 m, 2.7 m, 3.3 m schedule HOT DIP Galvanized steel with a 114mm OD and 2.2mm (wall) thickness of the tubing All metal components are to be finished with a baked on powder coat finish.With deck of size 1.45 x 1.45m and Staircase of size 1.5m x 0.77 m are fabricated from 2mm perforated solid punched steel. Deck perimeter is precision pre punched for attachments. Decks are pressed, punched, and welded sand blasted and vinyl plastic coated to a thickness of 4mm Along with Handrail of height 2.2 m and Dia 32 mm shall be an all-robotic welded unit, fabricated from 32 O.D. galvanized steel pipes with a baked on powder coating finish.Curved Slide of size 1.94 m x 1.85 m x 2.4 m, Panels,Toprails Of Monkey loop of size 1.8 m x 1.3 m.Deck of size 1.45 x 1.45m are fabricated from 2mm perforated solid punched steel. Deck perimeter is precision pre punched for attachments. Decks are pressed, punched, and welded sand blasted and vinyl plastic coated to a thickness of 4mm Roof of size Dia 2 m and height 0.82 m. Spiral Slide of size 1.16 m x 1.6 m x 3.6 m, Panels The rates are to be inclusive of supply and installation at site. Inclusive of All Taxes and Transportation Charges completion of the work as per direction of engineer in charge of work.	Each	1.00	0.00	2224684.00	0.00	1.00	2224684.00	2224684.00	1.00	2224684.00	

Scanned by TapScanner

60	of M.S. anchor bolts at each support with 10mm thick base plate and shoe plate. The work includes cutting, straightening, placing in position of M.S. pipes and welding wherever necessary and applying one coat of redoxide primer coat to all the. members including cost of all materials, labour charges, and hire charges of machineries for cutting, welding, grinding and erection equipments, with all lead and lift, transportation, complete as per specifications and directions of the Engineer in charge.	kg	39311.19	0.00	120.31	0.00	13667.90	120.31	1644385.53	13667.90	1644385.53	
61	Construction of embankment with approved material Gravel/Murrum with all lifts and leads, transporting to site, spreading, grading to required slope and compacting to meet requirement Table 300- 2 complete as per specifications.(Including cost of gravel / murrum, watering charges & compaction by vibratory roller to 95% of proctors density) MORTH Specification complete as per specifications and directions of the Engineer in charge	cum	246.58	0.00	354.20	0.00	0.00	354.20	0.00	0.00	0.00	
62	Providing and constructing non-load bearing wall with solid concrete blocks of size 400X100X200 having a block density not less than 1800kg/m3 having a minimum average compressive strength of 4.00 N/mm2 conforming to I.S : 2185 (Part 1) : 2005 and constructed with CM 1:4, as per IS 2572:2005 including cost of all materials, labour charges, scaffolding, curing, hire chargesof machineries etc., complete as per specifications. complete as per specifications and directions of the Engineer in charge.	Sqm	26.81	0.00	885.50	0.00	0.00	885.50	0.00	0.00	0.00	
63	Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners. wherever required smooth rendering, Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications complete as per specifications and directions of the Engineer in charge.	Sqm	462.73	0.00	283.94	0.00	0.00	283.94	0.00	0.00	0.00	
64	Providing 12mm thick cement plaster in single coat with cement mortar 1:4 , to brick masonry including rounding off corners wherever required smooth rendering, . Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications .complete as per specifications and directions of the Engineer in charge.	Sqm	545.69	0.00	222.34	0.00	0.00	222.34	0.00	0.00	0.00	
65	Providing rough cement plastering 15mm thick in single coat with cement mortar 1:4 to brick masonry for base of dadooing works with sand of approved quality, providing and removing scaffolding, incldng cost of materials, labour, curing complete as per specifications complete as per specifications and directions of the Engineer in charge.	Sqm	92.19	0.00	223.30	0.00	0.00	223.30	0.00	0.00	0.00	
66	Providing 12mm thick cement plaster in single coat with cement mortar 1:4 , to ceiling including rounding off corners wherever required smooth rendering, . including Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications.complete as per specifications and directions of the Engineer in charge.	Sqm	66.30	0.00	245.44	0.00	0.00	245.44	0.00	0.00	0.00	
67	providing applying two coats of wall putty to inside plastered walls and ceiling using white cement putty . Scrapping and levelling the surface using steel blade and preparing the surface even and smooth by using different grade sand papers, including cost of alll mateerial cost of labour and scaffolding etc .complete as per specification.complete as per specifications and directions of the Engineer in charge.	Sqm	605.09	0.00	84.70	0.00	0.00	84.70	0.00	0.00	0.00	
68	Providing and applying painting in two coats with plastic emulsion paint of approved brand on wall surface to give an even approved shade after thoroughly brushing the surface, free from mortar drops and other foreign matter including preparing the surface even and sand paper smooth, cost of materials, labour, complete as per specifications. - with primer complete as per specifications and directions of the Engineer in charge.	Sqm	545.69	0.00	98.18	0.00	0.00	98.18	0.00	0.00	0.00	

Scanned by TapScanner

78	the surface for the silicone to penetrate deeper into the concrete and leaving waterproofing applying polymer slurry made out of resin based acrylic / styrene / butadiene & cement in the ratio of 1:0.1, @0.50kg/sqm on the white surface, including all labour charges tools and equipments, all complete as per the specification and directions of the Engineer in charge.	Sqm	70.04	0.00	573.66	0.00	0.00	573.66	0.00	0.00	0.00	
79	Fixing of door frames in an existing opening including embedding frame in floor and walls after cutting masonary for holdfasts for embedding holdfast in cement concrete 1:3:6 of 20mm and downsize granite metal panning two coats of coal tar to sides of frame,making good the damages to walls and floor as required and disposal of the debries with lead upto 50 m. including cost of materials, labour, complete as per specifications and directions of the Engineer in charge.	Nos	4.00	0.00	1491.88	0.00	0.00	1491.88	0.00	0.00	0.00	
80	Providing Hiome wood frames of doors, windows, clerestory windows,ventilators and other frames, wrought, framed or assembled including making plaster groves (excluding cost of cement concrete and side clamps),but including cost of materials, labour, HOM of machineries complete as per specifications and directions of the Engineer in charge	cum	0.38	0.00	95616.68	0.00	0.00	95616.68	0.00	0.00	0.00	
81	Providing and fixing Frame/Hiome GRP Doorframe fabricated using E-Glass Chopped Strand Mat (CSM), UV-stabilized Isophalic Gelcoat and Isophalic resin. The thickness of the GRP door shall not be less than 3.0 mm. The doorframe consists of four segments, which are provided with plug-in-socket arrangement in-situ in the mould. The segments are plugged in and are joined together by means of screws. The GRP frame shall be provided with wooden reinforcement of 4 locations for high screw holding capacity for fixing metallic hold fast and shall be consolidated for fixing with medium density foam/Plaster with fibre reinforcement. Six Numbers of 50mmx25mmx5mm size U shaped 24 S. flat hold fast shall be provided with the frame complete as per specifications and directions of the Engineer in charge	m	22.80	0.00	490.88	0.00	0.00	490.88	0.00	0.00	0.00	

Scanned by TapScanner

	Description of Work	Unit	Tender Quantity	Previous Measurement			Present Measurement			Total to Date		
				Quantity	Rate	Amount	Quantity	Rate	Amount	Quantity	Amount	

Sl.No	Description of Work	Unit	Tender Quantity	Previous Measurement			Present Measurement			Total upto date		
				Quantity	Rate	Amount	Quantity	Rate	Amount	Quantity	Amount	Remarks
87	PROVIDING TRAPEZOIDAL PROFILED SHEET Providing and installing of pre painted Galvalume iron Trapezoidal profiled sheet of approved make 1060 mm width (1000 mm cover width), 28-30 mm crest height with crest distance of 200 mm c/c with 2 ribs at the centre for stiffening. The total coated thickness (TCT) of the sheet will be 0.47 mm +/- 0.02 mm tolerance Zinc-Alu Alloy coating AZ150 gsm as per ASTM 1397/A755-550 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 20-22 microns using self drilling/self tapping screws of 25 mm length, to be fixed over the existing purlins, rafters, channels and trusses complete as per specifications and directions of the Engineer in charge.	Sqm	1379.76	0.00	750.75	0.00	0.00	750.75	0.00	0.00	0.00	
88	Applying red lead ready mix priming coat over new steel or other metal surface including preparing the surface after throughly cleaning oil, grease, dirt and other foreign matter, and scoured with wire brushes, fine steel wool, sand papers including cost of materials, labour, complete as per specifications and directions of the Engineer in charge.	Sqm	1379.76	0.00	44.28	0.00	0.00	44.28	0.00	0.00	0.00	
89	Providing and installing of approved make pre painted Galvalume iron Accessories, like, plain, ridges, plain gutter, plain flashing, corner Trim, etc. The total coated thickness (TCT) of the sheet shall be 0.47 mm +/- 0.02 tolerance iron Zinc-Alu Alloy coating AZ 150 gsm as per ASTM 1397/755 -550 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 20-22 microns using self drilling / self tapping screws of 25 mm length. (width upto 500-600 mm only), to be fixed over the existing purlins, rafters, channels and trusses complete as per specifications and directions of the Engineer in charge.	Sqm	211.62	0.00	719.98	0.00	0.00	719.98	0.00	0.00	0.00	
90	Supply and installation of approved Wooden Floor for Indoor Hall - Maple Flooring with PU Sealer and coat polish 20mm thickness*60mm width*2000mm, third &better grade treated elements of size 30*60mm to be installed 30cm center to center 20mmm professional EPDM rubber pad inclusive of HOM, labour etc. complete as per specifications and directions of the Engineer in charge.	Sqm	531.36	0.00	15159.38	0.00	0.00	15159.38	0.00	0.00	0.00	

Scanned by TapScanner

Sl No	Description of Work	Unit	Tender Quantity	Previous Measurement			Quantity	Rate	Amount		
				Quantity	Rate	Amount					
101	Providing and fixing Chorinated Poly Venyl Chloride (CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all CPVC plain and brass threaded fittings including fixing the pipe with clamp at 1.00 mtr spacing. This includes jointing of pipes and fittings with one step CPVC solvent cement & the cost of cutting chases & making good the same including testing of joints complete. (Concealed work including cutting chases and good the walls etc.,)complete as per specifications and directions of the Engineer in charge.20mm nominal OD pipes	m	40.00	0.00	256.03	0.00	0.00	256.03	0.00	0.00	0.00
102	Providing and fixing Chorinated Poly Venyl Chloride (CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all CPVC plain and brass threaded fittings including fixing the pipe with clamp at 1.00 mtr spacing. This includes jointing of pipes and fittings with one step CPVC solvent cement & the cost of cutting chases & making good the same including testing of joints complete. (Concealed work including cutting chases and good the walls etc.,)complete as per specifications and directions of the Engineer in charge.25mm nominal OD pipes	m	40.00	0.00	319.55	0.00	0.00	319.55	0.00	0.00	0.00
103	Providing and fixing 453x357mm dia rectangular shape mirror with plastic moulded frame of approved make and shade with 6mm thick hard board backing including cost of materials, labour complete as per specifications and directions of the Engineer in charge.	Unit	2.00	0.00	1239.70	0.00	0.00	1239.70	0.00	0.00	0.00
104	Providing and fixing C.P brass towel rail 740mm length, 20mm dia with C.P brackets, fixed to wooden cleats with C.P brass screws including cost of materials, labour complete as per specifications and directions of the Engineer in charge.	Unit	2.00	0.00	806.58	0.00	0.00	806.58	0.00	0.00	0.00
105	Providing wash basin brackets of approved 1st qyuality and make confirming to ISI specifications and fixing for low down cistern as directed. Rate includes cost of materials and conveyance to work spot complete as per specifications and directions of the Engineer in charge	Pair	1.00	0.00	261.80	0.00	0.00	261.80	0.00	0.00	0.00
106	Constructing brick masonry inspection chamber 600x600mm, and 450mm depth, (clear inside dimension) for single pipeline, using table moulded non-modular bricks of class designation 50 in cement mortar 1:5, C.I cover withframe (light duty) 455x610mm internal dimensions, total weight of cover with frame to be not less than 38 kg (weight of cover 23kg and weight of frame 15 kg) R.C.C. top slab with cement concrete M 15 with 20mm and downsize granite metal, foundation concrete M 5 with 40mm and downsize granite metal inside plastering 12mm thick with cement mortar 1:3, finish smooth with a floating coat of cement on walls and bed concrete complete as per standard design including cost of materials, labour charges, curing complete as per specifications. Specification No. KBS 600x600mm and 450mm depth (clear inside dimension) for single pipeline, using table moulded non-modular bricks of class designation 50 in cement mortar 1:5, C.I cover withframe (light duty) 600x600mm. complete as per specifications and directions of the Engineer in charge.	NO	4.00	0.00	9265.99	0.00	0.00	9265.99	0.00	0.00	0.00
107	Providing of stoneware gully trap of approved quality and make fixing in M-15 and plastering with CM 1:3 wherever necessary (Rate includes cost of all). complete as per specifications and directions of the Engineer in charge 10 cms x 10 cms	Nos	2.00	0.00	206.94	0.00	0.00	206.94	0.00	0.00	0.00
108	Open Conduit System - supplying heavy gauge PVC conduit pipe dia mm thick comfirming to IS 2509 with suitable size bends, junction boxes, adhesive paste etc., and fixing using inverted wood plugs in case of RCC ceiling and RCC wall / stone structure or rawl plugs in case of brick walls and cement plastering the damaged portion using heavy gauge saddles at an interval of 700mm using NF screws)complete as per specifications and directions of the Engineer in charge. 19/20mm dia, 2mm thick	Mtr	133.00	0.00	50.05	0.00	0.00	50.05	0.00	0.00	0.00

Scanned by TapScanner

109	[illegible] plugs in case of RCC ceiling and RCC wall / stone structure or rawl plugs in case of brick walls and cement plastering the damaged portion using heavy gauge saddles at an interval of 70/6mm using NF screws.)complete as per specifications and directions of the Engineer in charge. 25mm dia, 2mm thick	Mtr	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]
110	Open Conduit System - supplying heavy gauge PVC conduit pipe dia. mm thick confirming to IS: 2509 with suitable size bends, junction boxes, adhesive paste etc. and fixing using inverted wood plugs in case of RCC ceiling and RCC wall / stone structure or rawl plugs in case of brick walls and cement plastering the damaged portion using heavy gauge saddles at an interval of 70/6mm using NF screws.)complete as per specifications and directions of the Engineer in charge. 32mm dia, 2mm thickk	Mtr	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]
111	Groove cutting : Supplying heavy gauge conduit PVC 25/2mm of s thick heavy with suitable size bend , metal junction boxes, adhesive pastes etc, by groove cutting in a wall and fixing by bracing U or J hooks and cement plastering up to the surface and run with 18SWG GI fish wire run throughout the conduit where ever necessary. complete as per specifications and directions of the Engineer in charge. 19/20mm dia, 2mm thick	Rmt	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]
112	Groove cutting : Supplying heavy gauge conduit PVC 25/2mm of s thick heavy with suitable size bend , metal junction boxes, adhesive pastes etc, by groove cutting in a wall and fixing by bracing U or J hooks and cement plastering up to the surface and run with 18SWG GI fish wire run throughout the conduit where ever necessary. complete as per specifications and directions of the Engineer in charge.25mm dia, 2mm thick	Rmt	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]
113	Groove cutting : Supplying heavy gauge conduit PVC 25/2mm of s thick heavy with suitable size bend , metal junction boxes, adhesive pastes etc, by groove cutting in a wall and fixing by bracing U or J hooks and cement plastering up to the surface and run with 18SWG GI fish wire run throughout the conduit where ever necessary. complete as per specifications and directions of the Engineer in charge. 32mm dia, 2mm thick	Rmt	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]
114	Point wiring using copper wire without switch (Class A material): Supplying and wiring adopting loop system in existing PVC conduit/casing capping using 2X0.5Sqmm(phase &Neutral) &1X0.5 Sqmm (Earth Wire) FRLSmultistrand PVC insulated 2x1.5Sqmm copper conffirming to the ISI)' With a 6Amps flurig type SP control switch shall be fixed on the existing plastic sheet / gang box the other end of the wire shall be terminated with sufficient loose length to a wood/PVC round block, complete for each outlet.Short point upto 3m complete as per specifications and directions of the Engineer in charge	Point	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]
115	Point wiring using copper wire without switch (Class A material): Supplying and wiring adopting loop system in existing PVC conduit/casing capping using 2X0.5Sqmm(phase &Neutral) &1X0.5 Sqmm (Earth Wire) FRLSmultistrand PVC insulated 2x1.5Sqmm copper conffirming to the ISI)' With a 6Amps flurig type SP control switch shall be fixed on the existing plastic sheet / gang box the other end of the wire shall be terminated with sufficient loose length to a wood/PVC round block, complete for each outlet.Medium point above 3m- 6m complete as per specifications and directions of the Engineer in charge	Point	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]	[illegible]

Scanned by TapScanner

	Wiring for lighting/power circuit using Grade using one of FRLS PVC insulated 1100 volts grade, multistrand copper with low conductor resistance single core wire in open or concealed system of wiring. With specified IS-694 confirming to Latest amendements 2.5sqmm. complete as per specifications and directions of the Engineer in charge.	Mtr	45.30	0.00	31.76	0.00	0.00	31.76	0.00	0.00	0.00	
	Wiring for lighting/power circuit using Grade using one of FRLS PVC insulated 1100 volts grade, multistrand copper with low conductor resistance single core wire in open or concealed system of wiring. With specified IS-694 confirming to Latest amendements 4sqmm. complete as per specifications and directions of the Engineer in charge.	Mtr	205.40	0.00	45.24	0.00	0.00	45.24	0.00	0.00	0.00	
	Supplying and fixing Metal Fan Box with Round Hook complete as per specifications and directions of the Engineer in charge.	Nos	4.00	0.00	86.63	0.00	0.00	86.63	0.00	0.00	0.00	
	Supplying and fixing of regular MCB distribution boards on wall/woodboard/flush mounting using required clamps, bolts, nuts etc , with provision for fixing suitable type capacity MCB'S single phase/ 3 phase / single door with powder coated painting made out of SWG MS enclosure 12 way SP & N complete as per specifications and directions of the Engineer in charge.	Each	5.00	0.00	1222.38	0.00	0.00	1222.38	0.00	0.00	0.00	
129	Supply and fixing minature circuit breakers on the existing MCB distribution boards using necessary fixing meterials and "C" type curve, Indiator ON/OFF energy cross -3 with as required confirming to IEC 60898.6-32 AMPS DP complete as per specifications and directions of the Engineer in charge.	Each	15.00	0.00	919.19	0.00	0.00	919.19	0.00	0.00	0.00	
130	Supplying, fixing and wiring earth electrode for grounding conduits , I.C. cutouts and others equipments on the meter board using 40mm dia 2.90mm long buried in a pit the pit should be filled with equal proportion of salt and charcoal 150mm all-round the pipe to complete depth. The connection from the pipe to the conduit ect, is to be established through GI wire of size as ISI specification 7.3.3 of IS 732 using 12mm dia bolt, nut, washers and check nuts ect the pipe shall have 16 through holes of 122mm dia, complete as per specifications and directions of the Engineer in charge.	No	1.00	0.00	3031.88	0.00	0.00	3031.88	0.00	0.00	0.00	
131	Supplying and running of GI/ copper strips for grounding connections, using necessary fixing materials as required.25 x 3mm G.I strip complete as per specifications and directions of the Engineer in charge.	Rm	91.56	0.00	75.08	0.00	0.00	75.08	0.00	0.00	0.00	
132	Supplying and fixing of slim box Fitting ,made out of CRCA sheet metal body with locking type holder completely wired Excluding Ballast &Flouresent Tube 1X4' Tube light Fitting complete as per specifications and directions of the Engineer in charge.	Nos	85.00	0.00	303.19	0.00	0.00	303.19	0.00	0.00	0.00	

Scanned by TapScanner

125	Supply and fixing of bakelite D.P. socket switch with/ without neon indicator over existing wood board or flush mounting in plastic plate switches as per IS 1293 and IS 3854 16Amps Combined switch and socket with indication complete as per specifications and directions of the Engineer in charge.	No	25.00	0.00	195.39	0.00	0.00	195.39	0.00	0.00	0.00	
126	Supply and fixing of bakelite D.P. socket switch with/ without neon indicator over existing wood board or flush mounting in plastic plate switches as per IS 1293 and IS 3854 Electronic stepped regulator complete as per specifications and directions of the Engineer in charge	Nos	8.00	0.00	212.71	0.00	0.00	212.71	0.00	0.00	0.00	
127	Wiring for lighting power circuit using Grade wiring one of FRLS PVC insulated 1100 volts grade, multistrand copper with low conductor resistance single core wire in open or concealed system of wiring. With specified IS-694, conforming to Latest amendements 2.5sqmm. complete as per specifications and directions of the Engineer in charge.	Mtr	45.30	0.00	31.76	0.00	0.00	31.76	0.00	0.00	0.00	
128	Wiring for lighting power circuit using Grade wiring one of FRLS PVC insulated 1100 volts grade, multistrand copper with low conductor resistance single core wire in open or concealed system of wiring. With specified IS-694, conforming to Latest amendements 4sqmm. complete as per specifications and directions of the Engineer in charge	Mtr	205.40	0.00	45.24	0.00	0.00	45.24	0.00	0.00	0.00	
129	Supplying and fixing Metal Fan Box with Round Hook complete as per specifications and directions of the Engineer in charge.	Nos	4.00	0.00	86.63	0.00	0.00	86.63	0.00	0.00	0.00	
130	Supplying and fixing of regular MCB distribution boards on wall/woodboard/flush mounting using required clamps, bolts, nuts etc., with provision for fixing suitable type capacity MCB'S single phase/ 3 phase, single door with powder coated painting made out of 18WG MS sheet(4 way SP & N complete as per specifications and directions of the Engineer in charge.	Each	5.00	0.00	1222.38	0.00	0.00	1222.38	0.00	0.00	0.00	
131	Supply and fixing miniature circuit breakers on the existing MCB distribution boards using required fixing materials and "C" type curve, Indicator ON/OFF energy cross -3 with as required conforming to IEC 60898,6-32 AMPS DP complete as per specifications and directions of the Engineer in charge.	Each	15.00	0.00	919.19	0.00	0.00	919.19	0.00	0.00	0.00	
132	Providing and laying earth electrode for grounding conduits, LC cutouts and others consisting of one pipe/ rod/ strip/ wood using 40mm dia 2.96mm long buried in a pit, the pit should be filled with a mixture of salt and charcoal 150mm all-round the pipe to complete depth. Connection from the pipe to the conduit ect, is to be established through GI wire of size as IEE regulations, 12mm dia bolt, nut, washers and check nuts ect, the pipe should be of 150mm dia, complete as per specifications and directions of the Engineer in charge.	No	1.00	0.00	3031.88	0.00	0.00	3031.88	0.00	0.00	0.00	
133	Providing and laying of copper strips for grounding connections, using necessary fixing materials complete as per specifications and directions of the Engineer in charge.	Rm	91.56	0.00	75.08	0.00	0.00	75.08	0.00	0.00	0.00	
134	Supply and fixing of Fan Fitting, made out of CRCA sheet metal body with locking type arrangement Silver 45 warmers Tube, 1X4' Tubc light Fitting complete as per specifications and directions of the Engineer in charge.	Nos	85.00	0.00	303.19	0.00	0.00	303.19	0.00	0.00	0.00	

Scanned by TapScanner

	charge.										
124	Supply and fixing of bakelite D.P. socket switch with/ without neon indicator over existing wood board or flush mounting in plastic plates/niches as per IS 1293 and IS 3854 Electronic stepped regulator complete as per specifications and directions of the Engineer in charge.	Nos	8.00	0.00	212.71	0.00	0.00	212.71	0.00	0.00	0.00
125	Wiring for lighting/power circuit using Grade using one of FRLS PVC insulated 1100 volts grade, multistrand copper with low conductor resistance single core wire in open or concealed system of wiring. With specified IS-694: confirming to Latest amendements 2.5sqmm. complete as per specifications and directions of the Engineer in charge.	Mtr	45.30	0.00	31.76	0.00	0.00	31.76	0.00	0.00	0.00
126	Wiring for lighting/power circuit using Grade using one of FRLS PVC insulated 1100 volts grade, multistrand copper with low conductor resistance single core wire in open or concealed system of wiring. With specified IS-694 confirming to Latest amendements 4sqmm. complete as per specifications and directions of the Engineer in charge.	Mtr	205.40	0.00	45.24	0.00	0.00	45.24	0.00	0.00	0.00
127	Supplying and fixing Metal Fan Box with Round Hook complete as per specifications and directions of the Engineer in charge.	Nos	4.00	0.00	86.63	0.00	0.00	86.63	0.00	0.00	0.00
128	Supplying and fixing of regular MCB distribution boards on wall/woodboard/flush mounting using required clamps, bolts, nuts etc , with provision for fixing suitable type capacity MCB'S single phase/ 3 phase / single door with powder coated painting made out of SWG MS enclosure 12 way SP & N complete as per specifications and directions of the Engineer in charge.	Each	5.00	0.00	1222.38	0.00	0.00	1222.38	0.00	0.00	0.00
129	Supply and fixing miniature circuit breakers on the existing MCB distribution boards using necessary fixing meterials and "C" type curve, Indiator ON/OFF energy cross -3 with as required confirming to IEC 60898 6-32 AMPS DP complete as per specifications and directions of the Engineer in charge.	Each	15.00	0.00	919.19	0.00	0.00	919.19	0.00	0.00	0.00
130	Supplying, fixing and wiring earth electrode for grounding conduits , I.C. cutouts and others equipments on the meter board using 40mm dia 2.90mm long buried in a pit. the pit should be filled with equal proportion of salt and charcoal 150mm all-round the pipe to complete depth. The connection from the pipe to the conduit ect, is to be established through GI wire of size as ISI specification 7.3.3 of IS 732 using 12mm dia bolt, nut, washers and check nuts ect. the pipe shall have 16 through holes of 122mm dia. complete as per specifications and directions of the Engineer in charge.	No	1.00	0.00	3031.88	0.00	0.00	3031.88	0.00	0.00	0.00
131	Supplying and running of GI/ copper strips for grounding connections, using necessary fixing materials as required 25 x 3mm G I strip complete as per specifications and directions of the Engineer in charge.	Rm	91.56	0.00	75.08	0.00	0.00	75.08	0.00	0.00	0.00
132	Supplying and fixing of slim box Fitting ,made out of CRCA sheet metal body with locking type holder completely wired Excluding Ballast &Flouresent Tube 1X4' Tube light Fitting complete as per specifications and directions of the Engineer in charge.	Nos	85.00	0.00	303.19	0.00	0.00	303.19	0.00	0.00	0.00

Scanned by TapScanner

	suitable to operate on 230V 50Hz supply complete as per specifications and directions of the Engineer in charge											
135	Fabricating supplying and mounting MS box made out SWG suitable for floor I wall mounting, fully weather proof with provision for better heat dissipation, provided with hinged front cover, equipped with tamper proof locking arrangements, with suitable size clamps with necessary cable entry pipe with gland and box should be finished with 2 coats of red oxide primer paint and finally finished with approved colour enameled metal paint etc , complete 14SWG	Sq cms	1.00	0.00	25265.63	0.00	0.00	25265.63	0.00	0.00	0.00	
136	Supplying ..... amps rated 3phase with neutral bus bar using required capacity electrolytic aluminum strips covered with heat shrinkable coloured PVC sleeve, mounted on phenolicsFRP/DMC insulator which are mounted on powder coated 40x6mm M.S.flat frame work in existing panel board. The bus bar shall have suitable holes for termination of incoming and outgoing cables as per IS specification with necessary bolts, nuts and washers etc., complete 1000Amps 4x75x10mm Alluminium Strips. complete as per specifications and directions of the Engineer in charge	Mtr	2.00	0.00	4884.69	0.00	0.00	4884.69	0.00	0.00	0.00	
137	Supplying and fixing angle iron frame work fabricated out of M.S. angle iron and M.S. flat with bolts, washers etc ,and painted with 2 coats of red oxide and then two coats of approved paint 75x75x6mm complete as per specifications and directions of the Engineer in charge	Mtr	4.00	0.00	481.25	0.00	0.00	481.25	0.00	0.00	0.00	
138	Supplying and fixing angle iron frame work fabricated out of M.S. angle iron and M.S. flat with bolts, washers etc ,and painted with 2 coats of red oxide and then two coats of approved paint 75x150x50x6mm C channel complete as per specifications and directions of the Engineer in charge	Mtr	4.00	0.00	654.50	0.00	0.00	654.50	0.00	0.00	0.00	
139	Supplying and Fixing Moulded Case Circuit Breaker (MCCB) over the existing wood/panel board using necessary screws, bolts, nuts and wiring complete, protection of Overload and Short circuit with thermal Magnetic/Microprocessed release and Earth Fault as per IS-13947.63/100Amps 25kA complete as per specifications and directions of the Engineer in charge	Each	1.00	0.00	5871.25	0.00	0.00	5871.25	0.00	0.00	0.00	
140	Supplying and fixing miniature circuit breakers on existing MCB distribution boards using necessary fixing materials and 'C' cure, indicator ON/OFF, energy cross-3 with Short circuit breaking cappacity of 10K and complete wiring as required Confirming to IEC 60898 40-63Amps TPN complete as per specifications and directions of the Engineer in charge	Each	8.00	0.00	1956.76	0.00	0.00	1956.76	0.00	0.00	0.00	
141	Supplying and fixing Trivector meter suitable for operation LT operation and CT operated meter in polycarbonate body in class 0 5accuracy as per IS 14697 and completely wired complete as per specifications and directions of the Engineer in charge	Each	8.00	0.00	3818.24	0.00	0.00	3818.24	0.00	0.00	0.00	
142	Supplying and fixing of LED type panel board indicating lamp with required colour suitable for 220v A.C 50 Hz 12/24v D.C complete as per specifications and directions of the Engineer in charge	Each	1.00	0.00	447.56	0.00	0.00	447.56	0.00	0.00	0.00	
143	Supplying, fixing and wiring 50/5 to 1000/5Amps 5VA burden Current Transformer Class 0.5 accuracy with Tape Wound complete as per specifications and directions of the Engineer in charge	Each	1.00	0.00	727.65	0.00	0.00	727.65	0.00	0.00	0.00	
144	Dismantling of barbed wire fencing / wire mesh fencing including posts, foundation concrete, back filling of pit by manual means including disposal of dismantled material with all lifts and stacking serviceable material and unserviceable material separately complete as per specifications MORTH Specification No 202 complete as per specifications and directions of the Engineer in charge	m	85.00	0.00	141.49	0.00	0.00	141.49	0.00	0.00	0.00	

Scanned by TapScanner

EIRL-1	KSR0315.1 Providing 20mm thick cement plaster in single coat with cement mortar to stone masonry & concrete surface including rounding off corners wherever required smooth rendering including providing and removing scaffolding ,cost of materials ,labour,curing etc complete as per specificatio.KSR015-3.12 do-cement mortar 1:6	Sqm			277.08	0.00	622.22	277.08	172390.89	622.22	172390.89	
EIRL-2	Earthwork excavation in all soil deposits and filling sides of foundation upto plinth in layers not exceeding 20cms ,in depth compacting each deposits layer by ramming after watering with all lead and lift including cost of all labour complete as per specification	cum			439.59	0.00	751.70	439.59	330438.92	751.70	330438.92	
EIRL-3	Fabricating, providing and erecting in poistion of M.S. Ornamental security Grill Gate without hot dip using 75 x 12mm M S Flat for alround frame work with verticals at the centre and horizontal centere support M S Square of 20 x20 mm of different heights as shown in the drawing are to be fixed at 16 cms C/C for square bars of full height and at 8cms C / C for bottom rods providing ornamental C 1 Designers at the bottom and C1 arrows in the midle and top. The entire frame work is to be fixed by means of expansion bolts to the brick pillars with necesary drilling holes, the work includes providing two coats of enamel painting over one coatr of red lead ready mix primer coat etc complete cost of all labour, painting, erection charges using hoist pulleycranes with all lead and lift, loading, transporting and unloading using hoist pulley cranes, scaffolding charges and all other incidental charges required for successful completion fo the work as per specification and drawings	Kg			142.56	0.00	1920.00	142.56	273715.20	1920.00	273715.20	
						Sub Total	0.00				59964980.16
						Add towards GST 12%	0.00				5264734.67
						Grand Total	0.00				65219714.84

Afthi
AE
24/03/2021

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner
